



Week 2

Tutorial: Project scope management, planning and scheduling

**UWE
Bristol**

University
of the
West of
England

Tutorial Activities

- Knowledge Check
- Effective and Fair Collaboration - Case study and Discussion
- Exercise 1: Scope Statement
 - Typical Scope Statement Example
- Exercise 2: Work Breakdown Structure (WBS) and Activity List
 - Typical WBS Example
- Exercise 3: Activity on Node Network and Critical Path



Group contract

Have you finalised and signed your group contract?



Knowledge check

Ready to test your knowledge?

Check out the **Knowledge Check** on Blackboard to test your understanding of the project management principles we covered in Weeks 1 and 2.

See how many you can get right, and good luck!




Effective and Fair Collaboration

Case study: Academic Group Project

1. What are the core problems presented in this scenario from the perspective of the hardworking students?
2. Why might be 'less motivated' students behave this way?
3. What are the immediate consequences for the group's performance and morale?



Group Discussion



Based on our discussion and your own experiences, brainstorm and develop practical solutions to make group projects in this class fairer and more effective. Consider solutions from three perspectives:

1. Student strategies: What can you do within your group to address issues like free-riding, unequal motivation, or conflict?
2. Tutor strategies: What can your tutor do to encourage fairer contributions and reduce common problems?
3. Assessment strategies: How can the grading system be designed to more accurately reflect individual contributions within a group context?

Class Discussion




Present your group's solutions and ideas to the class.

1. Which proposed solutions do you find most compelling and why?
2. Are there any solutions that seem problematic or difficult to implement?
3. How do these proposed solutions relate to teamwork in a professional setting?

*Peer assessment helps ensure fair recognition of individual contributions within the group project. Please refer to the **Peer Review - IPAC** guidance to understand how peer review will be applied in this module.*

Tutorial Activities

After Identifying the Project idea and the **potential solutions to the problem (challenge)**; **scope identification and planning** takes place

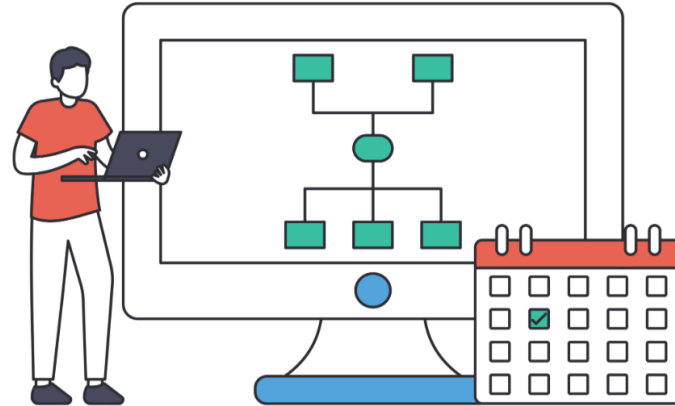


Typical Scope Statement Example

Project Name	IVR Project		
Project Sponsor	Dave Sponsor	Project Manager	Alice Michaels
Date of Project Approval	08 March 2015	Last Revision Date	08 March 2015
Scope Description	IN SCOPE: - An IVR system to handle and direct sales calls. - Setup of the IVR system ready to handle all sales enquiries - Training for the sales team on how to use the system - An administration system so the IVR system can be configured by the sales team OUT OF SCOPE: - Support for any other team other than sales - The ability to route complex sales enquiries, such as partnerships etc.		
Project Deliverables	- A customer facing IVR system - An IVR configuration system - A training manual for new and existing sales team members		
Acceptance Criteria	The project will be accepted when it is agreed by the sale team that the deliverables meet their needs (deliverables signed off). The project will also be considered a success if post launch testing shows that customer satisfaction is over 5 points higher than where it is now.		
Constraints	The sales team are not dedicated to this project, and must fit this around their day-to-day sales jobs.		
Assumptions	A sales team & full project team will be available to co-create the WBS		

Exercise 1: Within your group; formulate a Scope Statement for your project (20 min)

1. **Scope statement** involves determining all the work required to complete the project successfully within the agreed specifications and requirements
2. Main elements:
 - i. **Requirements:** The identification of stakeholders and technical requirements of your project
 - ii. **Scope description:** The definition of what is in and out of scope to avoid misunderstandings
 - iii. **Deliverables:** The end products that the project will produce
 - iv. **Acceptance criteria:** The conditions that must be met before project deliverables are accepted
 - v. **Constraints:** Restrictions that limit what the project can achieve
 - vi. **Assumptions:** The anticipated events or circumstances that are expected to occur during your project's life cycle

Typical WBS Example

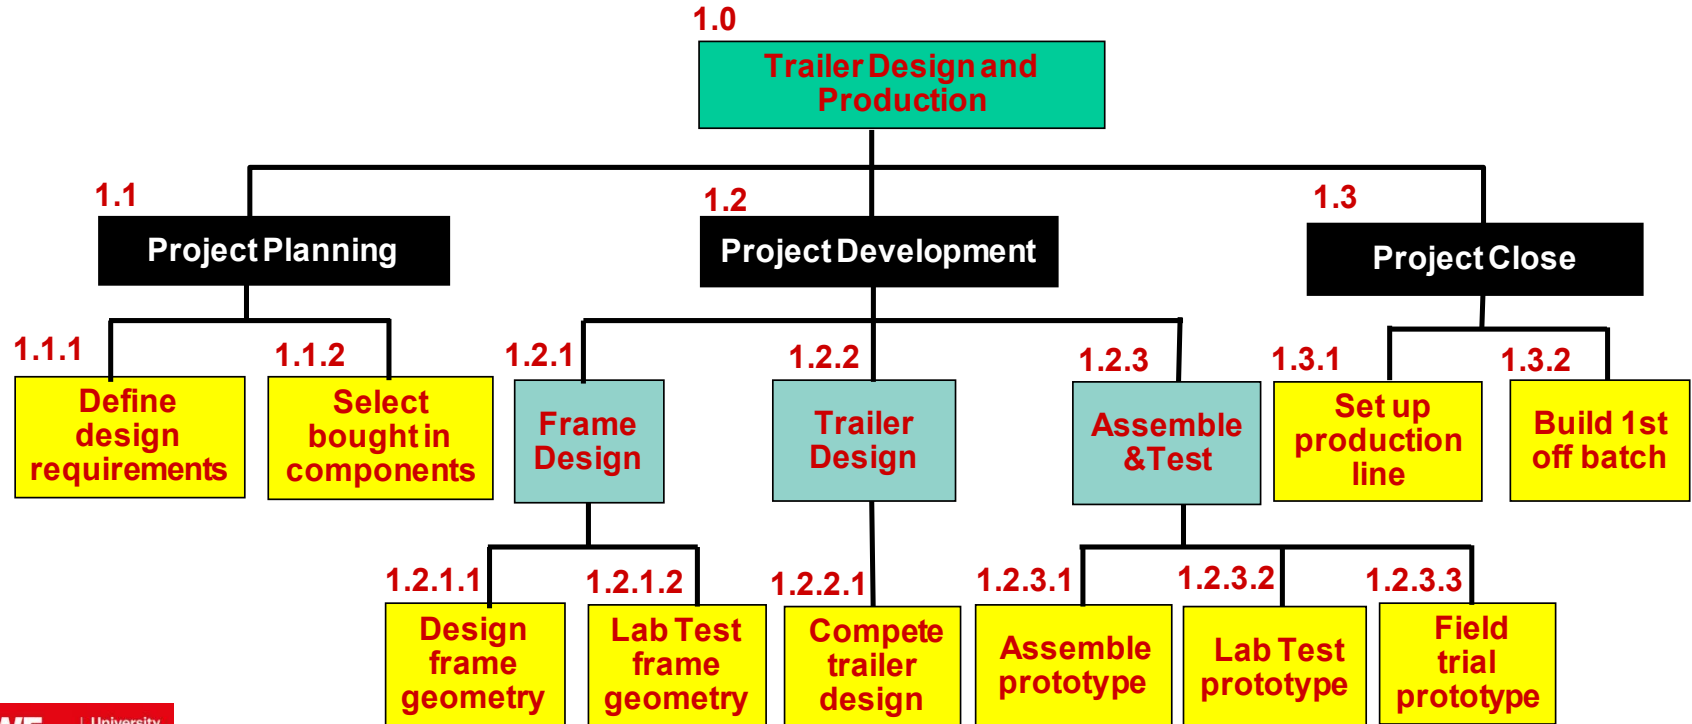

Activity List Example

Generate an **Activity List** from all activities at the bottom level of the WBS as indicated in the table below

Activity	Duration (weeks)	Preceding Activity(s)
1.1.1 Define design requirements	4	None
1.1.2 Select bought in components	4	1.1.1
1.2.1.1 Design frame geometry	2	1.1.1
1.2.1.2 Lab Test frame geometry	1	1.2.1.1
1.2.2.1 Compete trailer design	2	1.1.2 & 1.2.1.2
1.2.3.1 Assemble prototype	2	1.2.2.1
1.2.3.2 Lab Test prototype	1	1.2.3.1
1.2.3.3 Field trial prototype	2	1.2.3.2
1.3.1 Set up production line	4	1.2.2.1
1.3.2 Build 1st off batch	1	1.2.3.3 & 1.3.1



Exercise 2: Within your group; create WBS and Activity List for your project (15 min)

Work breakdown structure (WBS) divides the project into recognisable **tasks and activities** at different levels

- i. Level 1: Project
- ii. Level 2: Major tasks in the project
- iii. Level 3: Subtasks in the major tasks
- iv. Level 4: Activities to be completed (work packages)

Exercise 3:

Within your group; create Activity on Node Network and identify Critical Path (20 min)

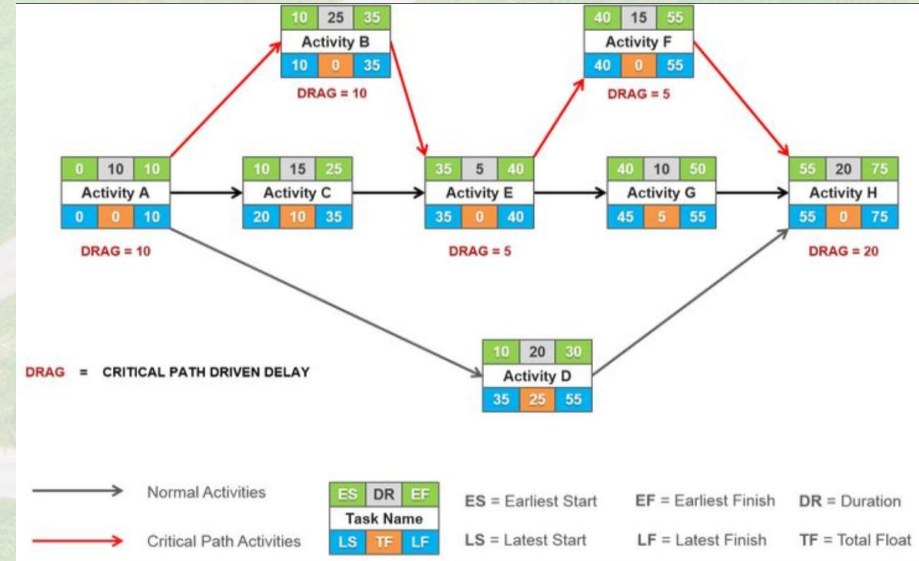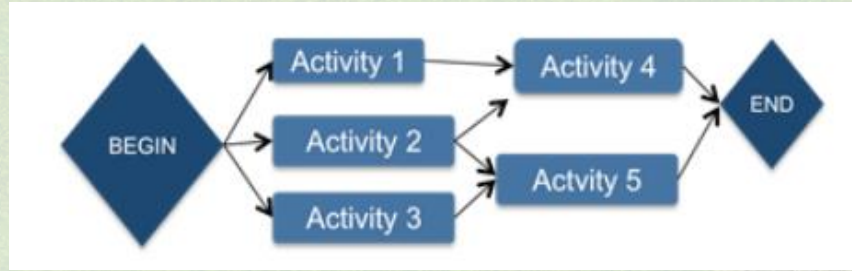

For more information, please follow the online pre – recorded lecture

Additional Resources:

[Scoping out a scope statement](#)

[WBS - PMI \(Project Management Institute\)](#)

- [1. How to draw a PDM network diagram](#)
- [2. Construct a PDM network diagram when given a table of dependencies](#)
- [3. Construct a table of dependencies when given a PDM network diagram](#)
- [4. Determine Early Start \(ES\) and Early Finish \(EF\) of activities in a network diagram](#)
- [5. Determine Late Start \(LS\) and Late Finish \(LF\) of activities in a network diagram](#)
- [6. Use forward and backward pass to determine project duration and critical path](#)

*Thank
you*

